

Relay service improvement case study

One page summary | Independent portfolio exercise | Version 1.0

A complete BA case study for improving routine IT fault handling in a fictional licensing support unit.

Problem and context

Email, phone and spreadsheet intake lead to missing information, unclear ownership and closure without verified restoration. The scenario reflects system operationalisation and public-sector service needs. It contains no real police, licensing, staff or applicant data.

Approach

Model seven stakeholder groups and six simulated findings; map current and future hand-offs; analyse seven gaps; define 12 prioritised requirements with acceptance criteria; map risks and governance; build and test a working service workflow; plan a controlled pilot and benefits review.

What is complete

A working browser prototype with structured intake, priority rules, assignment, controlled state changes, rejection and confirmed closure, searchable queue, CSV export and local event history. Fifteen automated domain checks and one browser integration review passed. Editable maps, requirements, test cases, controls, change plan and management briefing accompany the prototype.

Targets and evidence boundaries

Synthetic baseline: 50 faults, 12 minutes active handling per fault, 72% complete intake and 60% confirmed closure. Proposed targets: ≤ 6 minutes handling, $\geq 95\%$ completeness and 100% confirmed closure. Potential capacity: 5 hours per month at the assumed volume. No real benefits, stakeholder consultation, business UAT or production compliance are claimed.

Recommendation and release gates

Assess an existing approved service platform first. Consider an approved Microsoft 365 pilot only if required. Validate identity and permissions, privacy, classification, records, restore and support before live data. A four-week pilot and sponsor review determine whether to expand.

Tools: stakeholder analysis, swimlanes, gap matrix, BRD, stories, traceability, JavaScript prototype, versioned evidence and Microsoft 365 delivery blueprint. Role alignment: all nine QPS AO5 capabilities.

Stakeholders and problem analysis

Version 1.0 | 9 October 2026 | Fictional independent exercise

Problem statement: fragmented fault intake and unconfirmed closure create avoidable administration and uncertain service restoration. The proposed service gives staff one visible request, a named owner and a confirmed outcome.

Scope: routine device, access, application and network faults in three fictional licensing support units.
Exclusions: weapons licensing decisions, applicant records, exhibits, emergency response, security incident handling, live integrations, procurement and real staff data. Security or safety incidents must use authorised agency channels rather than this proposed routine workflow.

All seven stakeholder groups, six findings and the 50-fault baseline are simulated. In a real engagement, obtain informed participation, validate notes, invite dissent and triangulate interviews with observation and service data before baselining requirements.

Stakeholder map and engagement plan

ID	Stakeholder	Influence and impact	Needs	Engagement	Validation role
ST01	Frontline requesters	High impact / medium influence	Quick reporting; status visibility; assisted channel	Two 30-minute interviews and mobile task test	Validate required fields and confirmation wording
ST02	Service coordinator	High impact / high influence	One queue; fewer follow-ups; clear priorities	Process walkthrough and weekly design playback	Own triage rules and daily aged queue review
ST03	ICT technicians	High impact / high influence	Useful diagnosis; accountable hand-offs	Resolution workshop and exception testing	Validate routing, evidence and reopen rules
ST04	Unit manager and sponsor	High influence / medium impact	Operational continuity; defensible investment	Fortnightly decision brief and gate review	Approve scope, resources and residual risks
ST05	Privacy, security and records advisers	High influence / medium impact	Safe data handling; access; record lifecycle	Early assessment workshop and release review	Confirm applicable controls and evidence
ST06	Platform owner and external support provider	Medium influence / high impact	Reuse approved tools; support boundaries	Integration discovery and hand-off workshop	Confirm tenancy, licensing, contracts and support
ST07	Accessibility and staff representatives	Medium influence / high impact	Accessible reporting; fair workload; safe feedback	Keyboard task test and inclusive change sessions	Challenge barriers and review training options

Interview questions

- Walk me through your most recent fault, from detection to confirmation of recovery.
- Where do you wait, repeat information or ask another person for an update?
- What would make a fault urgent, and what workaround is available?
- Who owns each hand-off, and how do you know it has been accepted?
- What evidence is needed before closing or reopening a fault?
- What information is essential, restricted or unnecessary for this process?
- Which accessibility, shift, location or confidence barriers affect reporting?
- Which policy, integration and supplier constraints must we validate?
- What measure would convince you the new process is better?

Simulated interview findings

ID	Perspective	Fictional observation	Design implication	Evidence status
F01	Requester	I send another email because I cannot see whether anyone owns it.	Status visibility and an immediate reference	Simulated interview, not an actual quotation
F02	Coordinator	We re-enter the same fault into a spreadsheet, then ask for the missing location.	Structured intake and one queue	Simulated interview
F03	Technician	Urgent means something different to every person.	Agreed impact and urgency matrix	Simulated workshop
F04	Requester	The ticket was closed, but the printer still did not work.	Resolution evidence and explicit confirmation	Simulated interview
F05	Records adviser	A spreadsheet does not explain who changed a status and why.	Event history and controlled records export	Simulated workshop
F06	Staff representative	A web form cannot be the only way to get help.	Assisted intake and accessible task testing	Simulated interview

Success measures

The baseline below is an invented four-week sample of 50 faults, separate from the eight seeded prototype records. Targets are hypotheses to validate in a comparable four-week pilot. No operational benefits have been measured.

ID	Measure	Synthetic baseline	Proposed target	Measurement and owner
M01	Administrative handling time	12 minutes per fault	<= 6 minutes	Observed active minutes / completed faults; same definition before and after; coordinator; 4-week pilot
M02	Submission completeness	36 / 50 = 72%	>= 95%	Submissions accepted without clarification / all submissions; coordinator; weekly; assisted intake included
M03	Status-chasing contacts	22 / 50 = 44%	<= 20%	Faults with at least one status-only follow-up / all faults; coordinator; weekly
M04	Confirmed closure	30 / 50 = 60%	100%	Closed faults with explicit requester confirmation / all closed faults; process owner; weekly
M05	Operational guardrail	Not established	No service or accessibility deterioration	Track priority breaches, reopen rate and assisted-channel completion; establish baseline before pilot; sponsor

Assumptions and validation backlog


- A01: 50 routine faults per month and 12 minutes active handling per fault. Validate through a time-and-motion baseline; do not include technician repair time.
- A02: staff have an approved device and platform access. Confirm with the platform owner and include an assisted channel.
- A03: a business owner can define priorities and organise requester confirmation. Validate with all shifts and the coordinator.
- A04: existing approved service tooling may meet the need. Assess before building or procuring another platform.
- A05: policies, retention rules, real data classification and supplier arrangements are unknown. Obtain authoritative agency decisions before a pilot.

Current and future process analysis

Version 1.0 | 9 October 2026 | Fictional independent exercise


These simplified swimlanes show responsibilities and hand-offs; they are not asserted to be BPMN 2.0 compliant or to describe actual QPS processes. Open the SVG for a larger view, or edit the diagrams.net source.

Current state

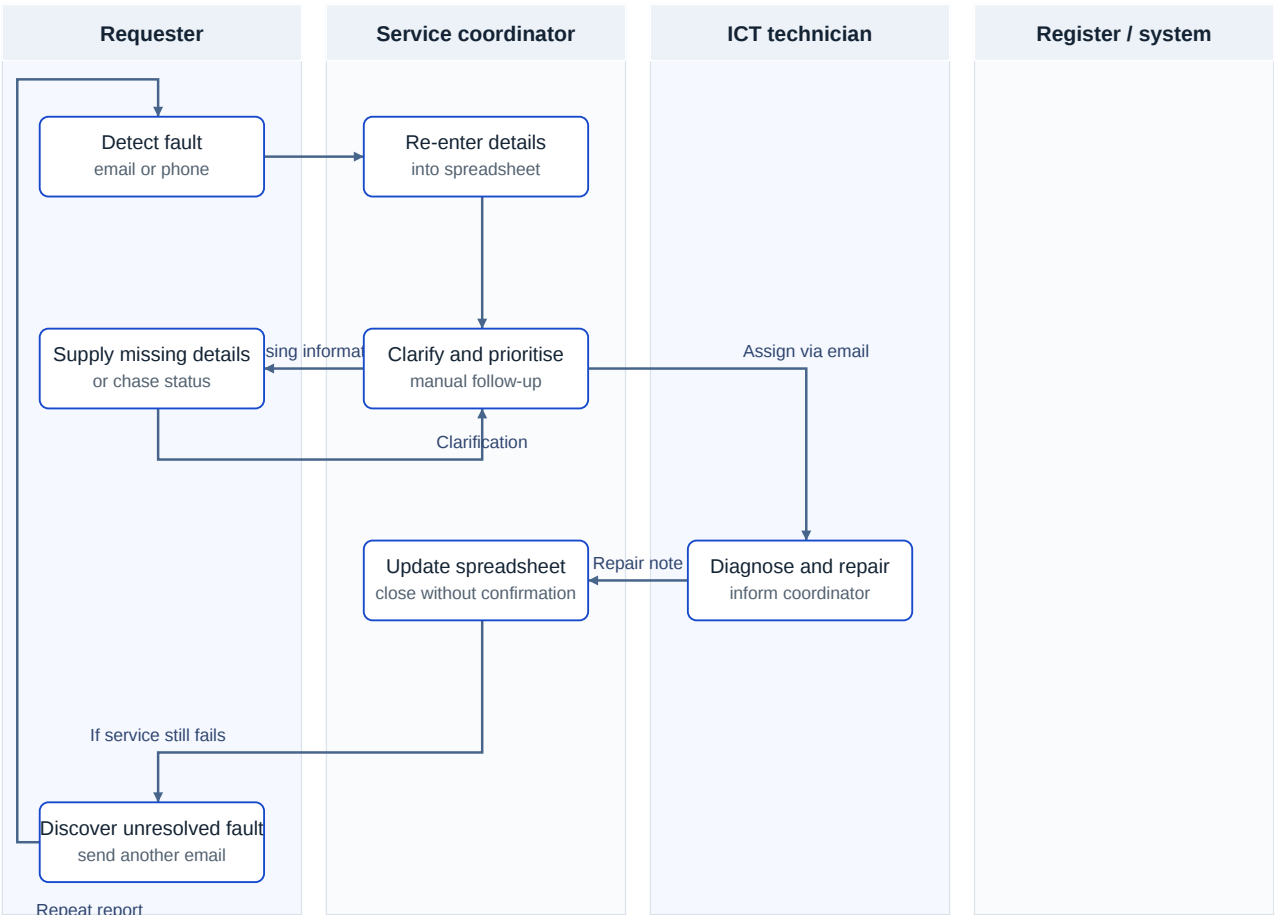

Invented current state for analysis; not an actual QPS process.
Spreadsheet updates have no dependable ownership or protected history.

Proposed future state

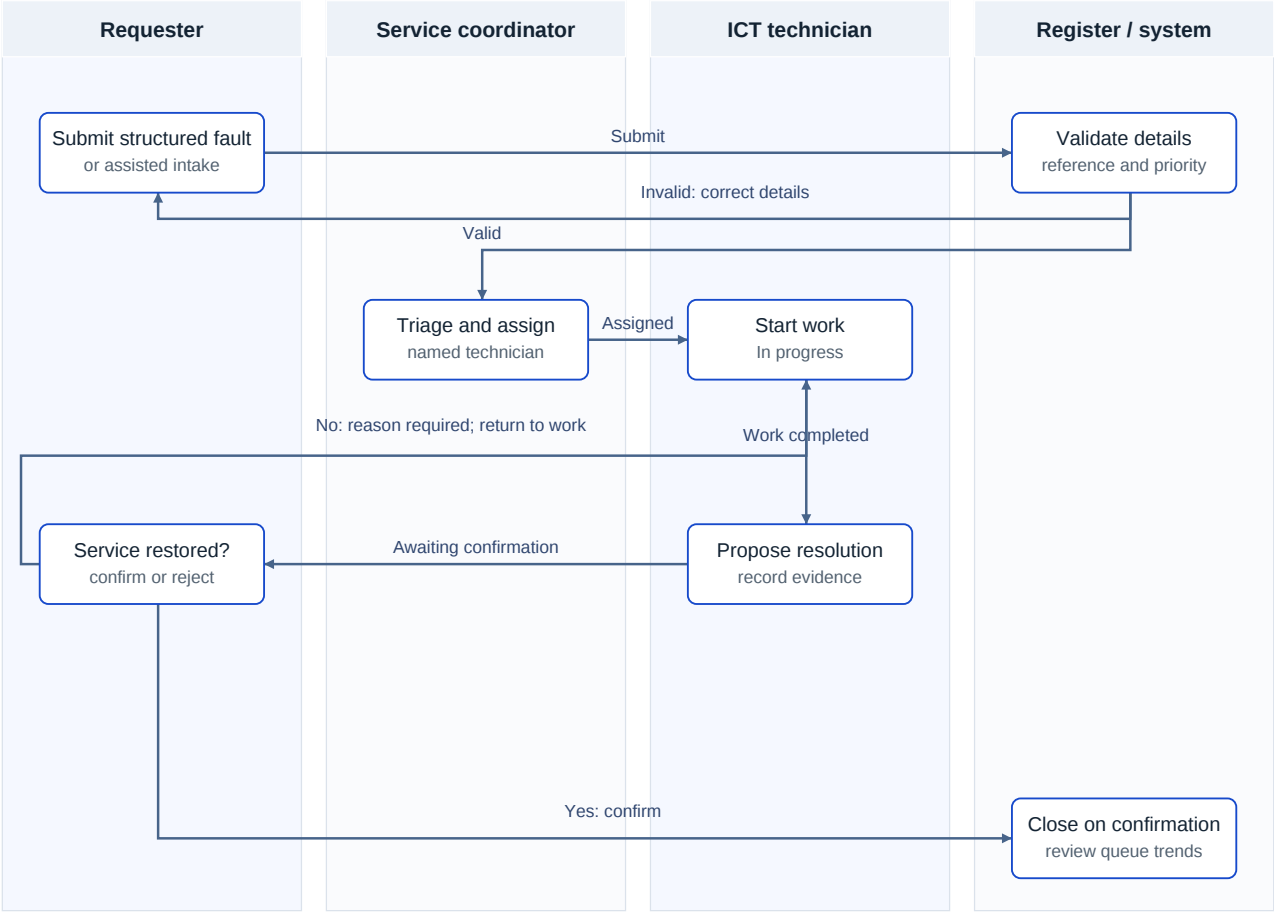

Proposed process. All state changes append a demo event.
Target timer continues while awaiting confirmation. No automatic closure.

Gap analysis

Gap	Current state	Problem or risk	Proposed improvement	Findings	Requirements	Measures
G01	Email, phone and spreadsheet intake	Incomplete information and duplicate entry	Structured form plus assisted intake in the same queue	F02, F06	R01, R10	M01, M02
G02	Unowned spreadsheet rows	Faults wait between teams	Named technician and visible state transitions	F01	R02, R03	M03
G03	Priority is self-selected	Unequal treatment and hidden operational risk	Impact and urgency matrix with visible due time	F03	R04	M05
G04	Closure by technician alone	Unresolved faults disappear from the backlog	Resolution evidence; requester confirms or rejects	F04	R05, R06	M04
G05	Overwritten spreadsheet cells	Weak accountability and unreliable reporting	Append event history; controlled export in target solution	F05	R07, R08	M05
G06	Review based on anecdotes	Repeated faults and benefits not evidenced	Queue measures and scheduled trend review	F01, F02	R09	M01, M03
G07	Unvalidated platform controls	Privacy, access and retention risks	Agency assessments and release gates before production	F05	R11, R12	M05

Priority definitions and timing are proposed business rules. High impact means multiple staff blocked; High urgency means no practical workaround. P1 = both High (4 elapsed hours); P2 = either High (24 hours); P3 = neither High (72 hours). The timer does not pause for confirmation. Capacity and escalation arrangements need sponsor validation.

Business requirements and traceability

Version 1.0 | 9 October 2026 | Fictional independent exercise

BRD purpose: define a testable service workflow for the fictional problem. Baseline version 1.0 is ready for portfolio review; business approval is not claimed. Must for pilot controls remain mandatory gates even though this prototype does not implement them.

Business outcomes and solution boundary

Reduce handling and chasing, improve submission quality and verify restoration. The working prototype is static HTML, CSS and JavaScript with a browser-local dataset. It demonstrates service behaviour, not production identity, protected audit, cross-device persistence or a deployed Microsoft 365 solution.

R01 · Must · Functional

As a requester, I want to submit a structured fault so that the coordinator has enough information to act.

Acceptance criteria: Given a new request, when title (5-120 characters), unit, category, impact, urgency and description (10-1000 characters) are valid, create a unique sequential reference and Submitted event. Reject blank or out-of-range values without saving.

Implemented in demo · Gap G01 · Tests T01, T02, T03

R02 · Must · Functional

As a coordinator, I want to assign a technician so that each accepted fault has an accountable owner.

Acceptance criteria: Given a Submitted fault and the Coordinator demo role, assigning a named technician moves it to Assigned and appends an event. Reject an empty technician or another role. Reassignment after submission is outside this prototype.

Implemented in demo · Gap G02 · Tests T04, T05

R03 · Must · Functional

As a technician, I want controlled state changes so that progress is meaningful and consistent.

Acceptance criteria: Only Assigned -> In progress and In progress -> Awaiting confirmation are permitted for the Technician demo role. Skip transitions are rejected without mutation.

Implemented in demo · Gap G02 · Tests T06, T07

R04 · Must · Business rule

As a coordinator, I want consistent priority rules so that faults are treated fairly.

Acceptance criteria: High impact and High urgency gives P1 with 4 elapsed hours; either High gives P2 with 24 hours; otherwise P3 with 72 hours. Due time is created time plus the target and never pauses while awaiting confirmation. These are proposed targets, not QPS SLAs.

Implemented in demo · Gap G03 · Tests T08

R05 · Must · Functional

As a technician, I want to record what restored service so that the requester can verify the result.

Acceptance criteria: Resolution requires 10-1000 characters and an In progress fault. Saving moves it to Awaiting confirmation with an event; a shorter note is rejected.

Implemented in demo · Gap G04 · Tests T09

R06 · Must · Functional

As a requester, I want to confirm or reject a resolution so that a fault closes only when service works.

Acceptance criteria: Only the Requester demo role can act on Awaiting confirmation. Confirming closes the fault and records closedAt. Rejecting with a reason of 10-1000 characters returns it to In progress, preserves prior events and clears closedAt. No automatic closure.

Implemented in demo; identity enforcement deferred · Gap G04 · Tests T10, T11

R07 · Must · Control

As a reviewer, I want a time-stamped event history so that hand-offs are explainable.

Acceptance criteria: Every successful creation and transition appends actor role, event, state and timestamp. Failed actions append nothing. The demo history is locally mutable; a production release needs server-managed identity and tamper-resistant records.

Demo history implemented; production assurance deferred · Gap G05 · Tests T12

R08 · Should · Functional

As a coordinator, I want a filtered CSV export so that I can review the same queue outside the app.

Acceptance criteria: Export exactly the filtered records with headers; quote commas, quotes and line breaks; prefix formula-like cells to prevent spreadsheet execution. Display fictional-data and local-storage notices.

Implemented in demo · Gap G05 · Tests T13

R09 · Should · Functional

As a manager, I want workload and completion measures so that I can identify pressure and trends.

Acceptance criteria: Display all-record counts for open, overdue, awaiting confirmation and closed faults. Open means every state except Closed; overdue is open and dueAt < demo clock. Search covers reference, title, unit and owner; status filters combine with search.

Implemented in demo · Gap G06 · Tests T14, T15

R10 · Must · Quality

As a staff member, I want a usable and inclusive service so that reporting does not depend on device or digital confidence.

Acceptance criteria: Provide labelled fields, keyboard-operable dialogs, visible focus, text status labels, a narrow-screen layout and an assisted-intake SOP. Conduct representative assistive-technology and user testing before release; full WCAG conformance is not claimed.

Basic UI checks executed; user validation deferred · Gap G01 · Tests T16, U01

R11 · Must for pilot · Security and privacy

As a security and privacy adviser, I want enforced access and assessed data handling so that operational information is protected.

Acceptance criteria: Before pilot, approve classification, privacy assessment, data location and supplier review; enforce SSO and server-side least privilege including ownership; test cross-user denial, logs and breach response. Role switching is only a demo convenience.

Production release gate; not implemented · Gap G07 · Tests U02

R12 · Must for pilot · Records and operations

As a records and platform owner, I want approved lifecycle and support controls so that records remain usable and service is recoverable.

Acceptance criteria: Before pilot, approve the applicable retention schedule without inventing a period; test restore, record export, support ownership, incident runbook and controlled deployment rollback. Keep requirements, decisions and releases versioned.

Production release gate; not implemented · Gap G07 · Tests U03

Data dictionary

Field	Type	Definition and validation
id	System-generated text	RF-1001 onwards; unique within the local demo dataset
title / description	Required text	5-120 / 10-1000 characters; synthetic details only
unit	Controlled list	Riverbend, Northbank or Lakeside; all fictional
category	Controlled list	Device, Access, Application or Network; no credentials
impact / urgency	Controlled lists	High or Standard; High impact = multiple staff blocked; High urgency = no practical workaround
priority / dueAt	Derived fields	P1/P2/P3 and UTC ISO timestamp; displayed as Australia/Brisbane
status / owner	Controlled state / alias	Submitted, Assigned, In progress, Awaiting confirmation, Closed; technician alias
resolution / closedAt	Text / optional timestamp	Resolution evidence retained across rejection; closure timestamp only on confirmation
events	Ordered event collection	Actor role, action, status, note and UTC time; local demonstration, not immutable audit

Requirements traceability matrix

Requirement	Gap	Priority	Test coverage	Delivery status
R01	G01	Must	T01, T02, T03	Implemented in demo
R02	G02	Must	T04, T05	Implemented in demo
R03	G02	Must	T06, T07	Implemented in demo
R04	G03	Must	T08	Implemented in demo
R05	G04	Must	T09	Implemented in demo
R06	G04	Must	T10, T11	Implemented in demo; identity enforcement deferred
R07	G05	Must	T12	Demo history implemented; production assurance deferred
R08	G05	Should	T13	Implemented in demo
R09	G06	Should	T14, T15	Implemented in demo
R10	G01	Must	T16, U01	Basic UI checks executed; user validation deferred
R11	G07	Must for pilot	U02	Production release gate; not implemented
R12	G07	Must for pilot	U03	Production release gate; not implemented

Microsoft 365 implementation blueprint

First assess the approved service management platform. If it cannot meet the need, test a low-code alternative in an approved tenant: Power Apps for intake, SharePoint or Microsoft Lists for the request register, a separate event list for state history, Power Automate for controlled notifications and escalation, and Power BI for trends. No tenant configuration or licensing has been performed in this portfolio.

- Design Request and RequestEvent lists with stable IDs, controlled choice columns, UTC timestamps and indexed filter fields; confirm delegation and realistic list volumes.

- Use agency SSO and group-based permissions; implement requester and assigned-technician restrictions in the data/service layer. Hiding controls in Power Apps is insufficient.

- Make state transitions server-validated and protect the event repository from end-user modification; use concurrency checks and idempotent flows to prevent duplicate events.

- Configure retention and record capture with the records owner; do not assume a SharePoint version history is sufficient. Validate tenant location, connector paths and supplier terms.

- Test notification failures, flow retries, backup/restore, operational support and licensing before pilot. The web demo does not send email or run automatic escalation.

Governance risk and compliance

Version 1.0 | 9 October 2026 | Fictional independent exercise

This is a control mapping and validation plan, not a compliance certification or legal interpretation. The current public sources were reviewed on 9 October 2026. Agency owners must confirm applicability and internal policy requirements.

QGEA | Use the current Queensland architecture policy catalogue to assess platform reuse and applicable policies. Confirm applicability with the agency architecture owner.

Required evidence: Architecture decision record; approved platform and integration assessment

Requirements: R11, R12

Sources: S01

IS18 current June 2026 | The current Information and cyber security policy uses lifecycle risk management and an ISO 27001 based ISMS. Map this project into agency assurance; this demo does not establish compliance.

Required evidence: Classification, access-control test, security assessment and accepted residual risks

Requirements: R11

Sources: S02

Information Privacy Act 2009 and QPPs | Use current Queensland Privacy Principles. Minimise personal data and assess collection, use, disclosure and transfers. Complete a privacy assessment before introducing actual staff or applicant data.

Required evidence: Privacy impact assessment, collection notice and breach response decision

Requirements: R11

Sources: S03, S04

Public Records Act 2023 | Create and manage appropriate records. Validate the applicable Queensland State Archives and agency retention and disposal requirements; no arbitrary retention period is proposed.

Required evidence: Records mapping, authorised retention decision and recoverable export

Requirements: R07, R12

Sources: S05

Customer experience and accessibility | QPS references the Queensland Digital Service Standard. Use needs research, clear status, assisted service and accessibility validation as design inputs.

Required evidence: Task observations, inclusive research, U01 and pilot feedback

Requirements: R10

Sources: S06

QPS ICT policies and practices | Internal policies were not supplied. Obtain the current authorised security, documentation, release and version-control requirements from accountable owners before implementation.

Required evidence: Agency-specific compliance checklist and release approvals

Requirements: R11, R12

Sources: Role document

Risk register

Likelihood and impact use 1-5 scales. Score = likelihood x impact; Low 1-4, Medium 5-9, High 10-25. Ratings are scenario estimates, not agency assessments. Residual High risks K02 and K07 remain unacceptable for production and are explicit release gates.

K01 | Operational or personal data entered into public demo

Inherent score: 3 x 5 = 15 High

Mitigation: Synthetic-only warning; no attachments; no network submission; reset local data

Owner: Project author

Residual score: 1 x 5 = 5 Medium

Acceptance or gate: Restrict the production intake and assess privacy before pilot

K02 | Demo role switch mistaken for access control

Inherent score: 4 x 5 = 20 High

Mitigation: Explicit role simulation label; R11 and cross-user denial test as pilot gate

Owner: Security lead

Residual score: 2 x 5 = 10 High

Acceptance or gate: Unaccepted for production; SSO and server enforcement required

K03 | Staff keep using separate email queues

Inherent score: $4 \times 3 = 12$ High

Mitigation: Champions, assisted intake, clear service channel and daily reconciliation

Owner: Process owner

Residual score: $2 \times 3 = 6$ Medium

Acceptance or gate: Pilot adoption must reach 80% before expansion

K04 | Wrong priority or unrealistic target

Inherent score: $3 \times 4 = 12$ High

Mitigation: Agree impact definitions; calibrate capacity; review breached high-priority faults daily

Owner: Coordinator

Residual score: $2 \times 3 = 6$ Medium

Acceptance or gate: Sponsor validates targets before pilot

K05 | Fault marked resolved while service is still unavailable

Inherent score: $3 \times 4 = 12$ High

Mitigation: Evidence plus requester confirmation; rejection returns to active work

Owner: ICT lead

Residual score: $1 \times 4 = 4$ Low

Acceptance or gate: Test T09-T11 and monitor reopen rate

K06 | Inaccessible interface or exclusion of shift staff

Inherent score: $3 \times 4 = 12$ High

Mitigation: Keyboard checks, assisted intake, recorded training plus captioned materials

Owner: Change lead

Residual score: $2 \times 3 = 6$ Medium

Acceptance or gate: Representative users must pass U01

K07 | Loss or alteration of records in browser storage

Inherent score: $4 \times 4 = 16$ High

Mitigation: State openly that demo storage is disposable; production repository and restore tests

Owner: Platform owner

Residual score: $3 \times 4 = 12$ High

Acceptance or gate: Unaccepted for production until U03 passes

K08 | Unsupported tenant, connector cost or data location

Inherent score: 3 x 4 = 12 High

Mitigation: Confirm approved platform, licensing, residency, supplier terms and support model

Owner: Platform owner

Residual score: 2 x 4 = 8 Medium

Acceptance or gate: No procurement or live tenant assumed

K09 | Misleading benefit or compliance claims

Inherent score: 3 x 4 = 12 High

Mitigation: Label invented baseline, proposed targets, executed checks and outstanding gates

Owner: Project author

Residual score: 1 x 4 = 4 Low

Acceptance or gate: Do not present prototype checks as stakeholder sign-off

Document control

Version	Date	Change	Status
0.1	9 Oct 2026	Scenario, findings and process baseline drafted	Superseded draft
0.9	9 Oct 2026	Prototype, requirements and governance mapped	Superseded draft
1.0	9 Oct 2026	Executed prototype tests and packaged portfolio evidence	Portfolio review baseline; no agency approval

Approver role	Decision required	Status
Project author	Portfolio baseline and disclosure accuracy	Prepared for review
Business sponsor	Scope, success measures, funding and residual risks	Not sought; fictional project
Security / privacy / records owners	Applicable controls and assessment evidence	Not sought; no agency implementation
Business UAT lead	Pilot acceptance and rollout readiness	Not executed

Version and change practice

Keep requirements, maps, decisions, source and test evidence in version control. A change request records problem, affected requirement IDs, benefit, risk, owner and acceptance impact. Assess it with the process owner, update traceability and tests, then baseline a reviewed release. Operational records require their own approved records repository; source control is not a substitute.

Decision log

ID	Decision	Reason	Status
D01	Use routine ICT faults in a fictional licensing unit	Align to system operationalisation while excluding operational licensing decisions	Project author; 9 Oct 2026
D02	Demonstrate local browser state only	Provide a complete low-friction interview workflow with synthetic data; no agency integration	Project author; 9 Oct 2026
D03	Require confirmation and allow rejection	Address false closure risk; no automatic closure timeout	Project author; 9 Oct 2026
D04	Prefer approved platform reuse	Limit bespoke support cost; conditional M365 pilot if existing platform is unsuitable	Proposed; sponsor validation pending
D05	Use fixed demo clock initially	Keep seed queue measures reproducible; advance the clock explicitly in the demo	Project author; 9 Oct 2026

Testing implementation and review

Version 1.0 | 9 October 2026 | Fictional independent exercise

Test plan: run a fresh synthetic dataset through submission, assignment, repair, rejection and closure. Check invalid inputs, role restrictions, event preservation, target calculations and export. Prototype results below were executed by the project author, not independent business users. They do not constitute organisational UAT.

Entry criteria: agreed requirements, versioned build and reproducible seed data. Pilot exit criteria: all Must and Must for pilot requirements passed in the target environment, zero Severity 1 (service/security failure) or Severity 2 (critical task blocked) defects, accessibility issues resolved and documented sponsor acceptance. Lesser defects need an owner and due date.

Executed prototype checks

T01 | Valid fault creates a Submitted request and initial event

Requirements: R01

Result: Pass

Execution method: Automated domain check

T02 | Invalid and whitespace input rejected without saving

Requirements: R01

Result: Pass

Execution method: Automated domain check

T03 | Unique references and assisted intake

Requirements: R01, R10

Result: Pass

Execution method: Automated domain check

T04 | Coordinator assignment records owner and event

Requirements: R02

Result: Pass

Execution method: Automated domain check

T05 | Empty owner and wrong-role assignment fail atomically

Requirements: R02

Result: Pass

Execution method: Automated domain check

T06 | Assigned fault can start only with Technician role

Requirements: R03

Result: Pass

Execution method: Automated domain check

T07 | Skipped or unknown transitions leave data unchanged

Requirements: R03

Result: Pass

Execution method: Automated domain check

T08 | All four priority combinations and target intervals

Requirements: R04

Result: Pass

Execution method: Automated domain check

T09 | Resolution requires adequate evidence and proper role

Requirements: R05

Result: Pass

Execution method: Automated domain check

T10 | Requester confirmation closes once and stamps closure

Requirements: R06

Result: Pass

Execution method: Automated domain check

T11 | Rejection requires reason, preserves history and returns to work

Requirements: R06

Result: Pass

Execution method: Automated domain check

T12 | Successful events retain roles, states and timestamps

Requirements: R07

Result: Pass

Execution method: Automated domain check

T13 | CSV quotes special characters and neutralises formula cells

Requirements: R08

Result: Pass

Execution method: Automated domain check

T14 | Snapshot queue counts and clock-driven overdue changes

Requirements: R09

Result: Pass

Execution method: Automated domain check

T15 | Search and status filters combine, with empty result

Requirements: R09

Result: Pass

Execution method: Automated domain check

T16 | Browser workflow, form labels and responsive review

Requirements: R01-R10

Result: Pass

Execution method: Verified submit -> assign -> start -> resolution -> reject -> second resolution -> confirmed closure; short resolution rejected; browser reset and reload preserved eight records; 390 px layout had no page overflow; all form fields labelled; Tab and Escape operated intake dialog. Not full WCAG or screen-reader validation.

Business UAT and production gates

U01 | Representative requesters including an assistive-technology user

Scenario: Complete submit, follow status and confirm or reject across mobile, keyboard and screen reader; assisted request enters same queue

Expected result: No critical task barrier; feedback resolved

Status: Not executed; representative users required

Requirements: R10

U02 | Security and privacy advisers

Scenario: Verify SSO; requester A cannot view or alter requester B records; technician access matches assignment; evaluate collection, logs and breach response

Expected result: No unauthorised access; signed assessment and residual-risk decision

Status: Not executable on browser-only demo

Requirements: R11

U03 | Records and platform owners

Scenario: Apply approved retention rules; export records; restore backup; deploy and roll back; verify incident hand-off

Expected result: Evidence meets approved records, recovery and support criteria

Status: Not executable until target platform exists

Requirements: R12

U04 | Process owner and nominated business testers

Scenario: Repeat T01-T16 in the target platform and exercise interruption, duplicate reports and supplier hand-off

Expected result: All Must requirements pass; no open Severity 1 or 2 defects

Status: Planned; no business acceptance claimed

Requirements: R01-R10

Change communications and rollout

Stage	Accountable owner	Activity	Gate
Discover / week 1	Process owner and BA	Validate baseline and workflow with all shifts; include accessibility and supplier voices	Research notes agreed; scope and outcome definitions approved
Design / week 2	BA, platform owner and advisers	Playback requirements; challenge priority rules; assess approved platform reuse	Requirements baseline and privacy, security, records assessments completed
Validate / week 3	ICT and representative users	Complete UAT including exceptions, permission denial and restore; train champions	All Must for pilot requirements passed and residual risks accepted
Pilot / weeks 4-7	Process owner and change lead	Small volunteer unit; 20-minute role-based sessions; captioned guide; assisted channel; daily triage	80% channel adoption; no critical service, privacy or accessibility issue
Review / week 8	Sponsor and BA	Compare like-for-like baseline; inspect incidents and feedback; decide expand, revise or stop	Written review and sponsor decision; no automatic expansion

Audience	Message	Channel and timing	Feedback
All shifts	Why the change matters; how to report; assisted help remains available	Sponsor announcement before pilot; team briefing and captioned quick guide	Short task observation and anonymous issue channel
Coordinators and technicians	Priority definitions, ownership, rejection and exception handling	Role-based workshop before pilot; daily 10-minute triage during week 1	Record process issues and triage conflicts
Manager and advisers	Performance, incidents, adoption and control readiness	Weekly pilot note and gate review	Explicit accept, revise or stop decision

Training and support

Use a 20-minute hands-on session for each role: requesters submit and confirm; coordinators triage and assist; technicians record evidence and handle rejection. Provide a one-page illustrated guide, captioned recording, shift-friendly repeats and named champions. Publish safe escalation channels and support hours agreed with the platform owner.

Cutover and rollback

Before cutover, reconcile open faults to unique references, assign owners, test access and restore, publish support details and stop dual entry. Keep the prior approved register available read-only. If access failures block critical work, a serious privacy/security event occurs or records cannot be recovered, the process owner pauses intake, returns to the approved fallback channel, reconciles changes and seeks sponsor authority before restarting. Never roll back by deleting operational records.

Post implementation review plan

No operational implementation or PIR has occurred. At the end of the proposed four-week pilot, compare M01-M05 with an agreed like-for-like baseline, segment by priority and assisted intake, inspect outliers and reopen causes, and report adoption and unresolved control issues. The sponsor decides expand, refine or stop at week 8. A 30/60/90-day benefits review follows only if rollout proceeds.

Continuous improvement and working agreement

Maintain an improvement backlog linking feedback to gaps and requirements. Hold a weekly retrospective, rotate demonstrations, invite respectful challenge and record decisions without blame. Include all shifts and accessibility needs, share documentation, manage workload fairly and use safe channels for sensitive concerns. These are proposed team practices, not claims of previous employment performance.

Advice to management

Version 1.0 | 9 October 2026 | Fictional independent exercise

To: fictional Unit Manager. From: portfolio project author. Date: 9 October 2026. Decision sought: approve a short discovery and controlled pilot design, subject to platform, privacy, security and records assurance. This is a simulated briefing, not a real funding request.

Recommendation

Assess the existing approved service platform first. Configure it if it meets the requirements. If it does not, design a limited Microsoft 365 pilot in an approved tenant after R11 and R12 pass. Use the current web application only to validate workflow and requirements; it is not a production deployment recommendation.

Issue and evidence

The fictional unit handles faults across emails and spreadsheets, with duplicated handling, unclear ownership and closure without requester confirmation. Six simulated findings and a synthetic sample of 50 faults support the design exercise. Actual service data and stakeholder validation are required before investment decisions.

Options appraisal

A | Improve the spreadsheet

Advantages: Low effort; immediate template and ownership rules

Risks and dependencies: Still fragmented; weak automation, permissions and records evidence

Assessment: Interim fallback only

B | Configure an existing approved service platform

Advantages: Reuse identity, support, record lifecycle and reporting capabilities

Risks and dependencies: Availability, licensing, configuration and integration must be established

Assessment: Preferred after discovery confirms fit

C | Microsoft 365 low-code pilot

Advantages: Microsoft Lists or SharePoint, Power Apps and controlled Power Automate flows

Risks and dependencies: Item permissions, delegation, connector licensing, audit and records design need validation

Assessment: Conditional pilot if option B cannot meet needs

D | Commission a custom production application

Advantages: Maximum workflow flexibility

Risks and dependencies: Highest delivery, assurance and ongoing support burden

Assessment: Do not recommend at this stage

Benefits and indicative effort

At 50 faults per month, reducing active administrative handling from 12 to 6 minutes would release $50 \times 6 / 60 = 5$ staff hours per month. At an assumed loaded rate of A\$65 per hour, this represents A\$325 per month or A\$3,900 per year in potential capacity value, not cash savings. At 25-100 faults per month, the same assumption gives 2.5-10 hours per month. The synthetic baseline does not establish demand or a return on investment.

Allow an indicative 8-12 person-days for discovery, configuration, assessment, testing and training, before licensing, integration or remediation. At the same assumed rate and 7.6-hour day this is A\$3,952-A\$5,928 in effort. This is an estimate for comparison, not a quote; benefit alone does not yet justify custom development.

Risks conditions and next decision

Primary risks are improper access, uncontrolled records, adoption failure and misleading priorities. Confirm platform fit, classification, privacy, retention, support and access denial before any live pilot. Residual High risks for demo access and storage remain unaccepted for production. Measure completeness, handling, chasing, confirmation and service guardrails during the pilot. Expand only after a documented sponsor review; stop or revise if safety, security, accessibility or service quality deteriorates.

Recruiter walkthrough and capability mapping

Version 1.0 | 9 October 2026 | Fictional independent exercise

A five-minute walkthrough

Time	Show	Explain
0:00-0:45	One-page summary	Fictional problem, scenario boundaries and the proposed outcomes
0:45-1:30	Current/future maps and one gap	Follow G04 through R05/R06 to T09-T11
1:30-3:30	Prototype lifecycle	Submit, assign, resolve, reject, then confirm; inspect the history
3:30-4:15	Governance and tests	Distinguish demonstrated behaviour from outstanding production gates
4:15-5:00	Management briefing	Recommend reuse; explain the conditional benefit model and pilot decision

All nine role capabilities

#	Role requirement	Portfolio evidence	Interview emphasis
1	Coordinate and improve IT systems and BA	F01-F06; G01-G07; R01-R12; working prototype	Translate fragmented work into a controlled service workflow
2	Develop and support change management	Change plan; training guide; pilot and rollback criteria	Include shift staff, champions, assisted reporting and support ownership
3	Determine requirements within legislative, IT and customer frameworks	BRD; acceptance criteria; data dictionary; governance mapping	Identify policy constraints and validate internal rules with owners
4	Adhere to IT policies, security, documentation and version control	R11-R12; risk register; decision log; document control	Make unimplemented assurance controls explicit release gates
5	Advise management on improvement, innovation and risk	Two-page briefing; options appraisal; benefit model	Recommend reuse before custom build and avoid overstated savings
6	Analyse, document, develop, test, deliver, implement and review	Process maps; traceability; demo; executed tests; rollout and PIR plan	Separate completed prototype work from proposed organisational rollout
7	Engage operational and business stakeholders	Stakeholder map; questions; engagement plan; validation backlog	Explain the engagement approach; interviews in this project are simulated
8	Identify improvements and current/future gaps	Editable swimlanes; gap analysis; linked measures	Trace each change to a bottleneck, requirement and test
9	Contribute to an ethical, inclusive and improving team	Working agreement; accessible service; feedback and learning loop	Invite challenge, share knowledge and avoid inventing actual leadership experience

STAR answer for this portfolio exercise

Situation: "For an independent portfolio exercise, I modelled a fictional licensing support unit where IT faults were handled across email and a spreadsheet." Task: "I set out to demonstrate an end-to-end BA approach to reducing administrative effort and improving confirmed restoration." Action: "I created simulated stakeholder findings, mapped the hand-offs, traced gaps into testable requirements, built the workflow and documented the assurance and change gates." Result: "I delivered a working prototype and executed domain checks. The benefit targets remain hypotheses; a real pilot would validate them."

Team leader behaviour without invented experience

The supplied role identifies the Team leader stream. Use the decision log to explain how you would lead a project without direct reports: agree outcomes, invite challenge, communicate trade-offs, support learning, manage risks and hold decision owners accountable. Pair this exercise with truthful examples from your own work when addressing previous performance.

Application context

The supplied role description is Business Analyst AO5, Weapons Licensing Group, Legal Division, Brisbane, QLD/702780/26. It lists Tuesday 13 October 2026 as the closing date and seeks strong change management, process mapping and Microsoft Suite experience. The role document and applicant guide request a statement of no more than two A4 pages and a current CV. Treat the portfolio as supporting evidence; the written statement needs genuine previous-performance examples. These application details are taken from the supplied documents and have not been reverified against a live advertisement.

Sources assumptions and downloads

Version 1.0 | 9 October 2026 | Fictional independent exercise

Public framework references were checked on 9 October 2026. The attached recruitment documents were used as source material for role alignment, not as instructions to carry out application actions. No application, email or stakeholder communication has been submitted.

S01 · QGEA policy catalogue Official framework catalogue; confirm applicability at design gate

[Open official source](#)

S02 · Information and cyber security policy IS18 Current v10.0.0; effective June 2026; checked 9 October 2026

[Open official source](#)

S03 · OIC privacy reform information QPP reforms commenced 1 July 2025; checked 9 October 2026

[Open official source](#)

S04 · OIC privacy impact assessments Current privacy assessment guidance; checked 9 October 2026

[Open official source](#)

S05 · Public Records Act 2023 Official Queensland legislation; current version checked 9 October 2026

[Open official source](#)

S06 · QPS Digital Service Standard Official QPS customer experience context; checked 9 October 2026

[Open official source](#)

Supplied role documents

702780-26-Role Description.docx and 702780-26-Applicant Guide non-Police.docx, supplied by the applicant. Original files and contact details are not copied into the hosted portfolio.

Download and reuse

- Portfolio pack: summary, discovery, maps, requirements, controls, testing, change, management advice and interview material.
- Editable draw.io maps and SVG exports; CSV traceability, risk, gap and UAT registers; Markdown evidence source and prototype source.
- All names, units, operational scenarios, interview findings and baseline figures are fictional. No QPS logo, approval or affiliation is claimed.

Detailed test procedure appendix

Self-executed prototype checks on 9 October 2026. The result register and runnable test source are included in the editable evidence ZIP.

T01 | Valid fault creates a Submitted request and initial event

Requirements: R01 | **Result:** Pass

Preconditions: Fresh sample

Steps: Submit valid title, description and controlled fields

Expected and observed: Unique reference, Submitted status and initial event

T02 | Invalid and whitespace input rejected without saving

Requirements: R01 | **Result:** Pass

Preconditions: Fresh sample

Steps: Submit whitespace, short text, overlong title and invalid unit or urgency

Expected and observed: Each fails; dataset unchanged

T03 | Unique references and assisted intake

Requirements: R01, R10 | **Result:** Pass

Preconditions: Fresh sample

Steps: Submit twice as Requester and Coordinator; attempt as Technician

Expected and observed: Unique references; assisted intake labelled; Technician denied

T04 | Coordinator assignment records owner and event

Requirements: R02 | **Result:** Pass

Preconditions: Submitted fault

Steps: Assign Alex T. as Coordinator

Expected and observed: Assigned status, named owner and appended event

T05 | Empty owner and wrong-role assignment fail atomically

Requirements: R02 | **Result:** Pass

Preconditions: Submitted fault

Steps: Attempt empty owner and Requester assignment

Expected and observed: Rejected; state and history unchanged

T06 | Assigned fault can start only with Technician role

Requirements: R03 | **Result:** Pass

Preconditions: Submitted then assigned fault

Steps: Start work as Technician

Expected and observed: In progress; third event

T07 | Skipped or unknown transitions leave data unchanged

Requirements: R03 | **Result:** Pass

Preconditions: Submitted fault

Steps: Attempt start, resolve, confirm and unsupported delete

Expected and observed: Rejected; state unchanged

T08 | All four priority combinations and target intervals

Requirements: R04 | **Result:** Pass

Preconditions: Fresh sample for each combination

Steps: Submit all four High/Standard impact and urgency combinations

Expected and observed: P1 4h, P2 24h, P2 24h, P3 72h

T09 | Resolution requires adequate evidence and proper role

Requirements: R05 | **Result:** Pass

Preconditions: In progress fault

Steps: Try short evidence and wrong role; then valid resolution as Technician

Expected and observed: Invalid attempts denied; valid resolution awaits confirmation

T10 | Requester confirmation closes once and stamps closure

Requirements: R06 | **Result:** Pass

Preconditions: Awaiting confirmation

Steps: Attempt Technician confirmation; confirm as Requester; repeat

Expected and observed: Only Requester closes; closedAt set; repeated confirmation denied

T11 | Rejection requires reason, preserves history and returns to work

Requirements: R06 | **Result:** Pass

Preconditions: Awaiting confirmation

Steps: Reject with short then valid reason; resolve again and confirm

Expected and observed: Short reason denied; valid rejection returns to work and preserves history; eventual closure succeeds

T12 | Successful events retain roles, states and timestamps

Requirements: R07 | **Result:** Pass

Preconditions: Progressed request

Steps: Read every event; attempt invalid confirmation

Expected and observed: Role, state and timestamp retained; invalid action adds no event

T13 | CSV quotes special characters and neutralises formula cells

Requirements: R08 | **Result:** Pass

Preconditions: Seed queue and special text

Steps: Filter Northbank; export; exercise commas, quotes, line breaks and formula prefix

Expected and observed: Only filtered requests; CSV escaped; formula text neutralised

T14 | Snapshot queue counts and clock-driven overdue changes

Requirements: R09 | **Result:** Pass

Preconditions: Seed queue at starting clock

Steps: Read counts; advance 24h; attempt invalid clock advance

Expected and observed: 6 open, 2 overdue, 1 awaiting, 2 closed; overdue becomes 4; invalid advance denied

T15 | Search and status filters combine, with empty result

Requirements: R09 | **Result:** Pass

Preconditions: Seed queue

Steps: Search Riverbend + Submitted, reference, owner and absent text

Expected and observed: 2 combined matches; reference 1; owner 2; absent text 0
